Appendix no. 3 Real property acquisition schedule

Construction of “Krosnowice” - a dry flood control reservoir on Duna Stream

11.02.2016

ID	Nazwa zadania	Start	Finish
1	**2A.2/2/2015 Construction of “Krosnowice” - a dry flood control reservoir on Duna Stream**	**2015-07-13**	**2017-03-30**
2	**Resettlement Action Plan (RAP) Krosnowice**	**2015-07-13**	**2017-03-30**
3	Identification of properties necessary for implementation of the project – Krosnowice	2015-07-13	2016-05-10
4	Social and economic research	2015-08-06	2015-09-20
5	Development of social and economic study	2015-09-20	2016-05-20
6	Consultations with local society and with owners of properties to be expropriated	2015-11-05	2016-09-30
7	Obtainment of IPIP (Investment project implementation permit)	2016-12-30	2016-12-30
8	Evaluation of land properties	2016-11-14	2016-12-30
9	Development of LA&RAP (RAP) Land Acquisition and Resettlement Action Plan	2015-10-09	2016-05-20
10	Provision of a draft LA&RAP (RAP) to the Employer	2016-05-20	2016-05-20
11	Updates, corrections	2016-05-20	2016-08-16
12	Obtainment of the World Bank’s “OK”	2016-08-16	2016-08-25
13	Public hearings on a draft LA&RAP (RAP)	2016-09-23	2016-10-19
14	Development of LA&RAP (RAP) including conclusions drawn from the public discussion	2016-10-19	2016-11-21
15	Obtainment of the World Bank’s NO	2016-11-21	2016-12-05
16	Negotiations with PAP (Project Affected Person (s)) on the compensation value	2016-12-30	2017-02-28
17	Transfer of the case to the Voivod (in case negotiations failed)	2017-02-28	2017-02-28
18	Issuance of a decision by the Voivod on the compensation value	2017-02-28	2017-03-30
19	Handing over the properties physically by the PAP to the Investor	2017-01-06	2017-03-09
20	Payment of compensation	2017-01-06	2017-03-30

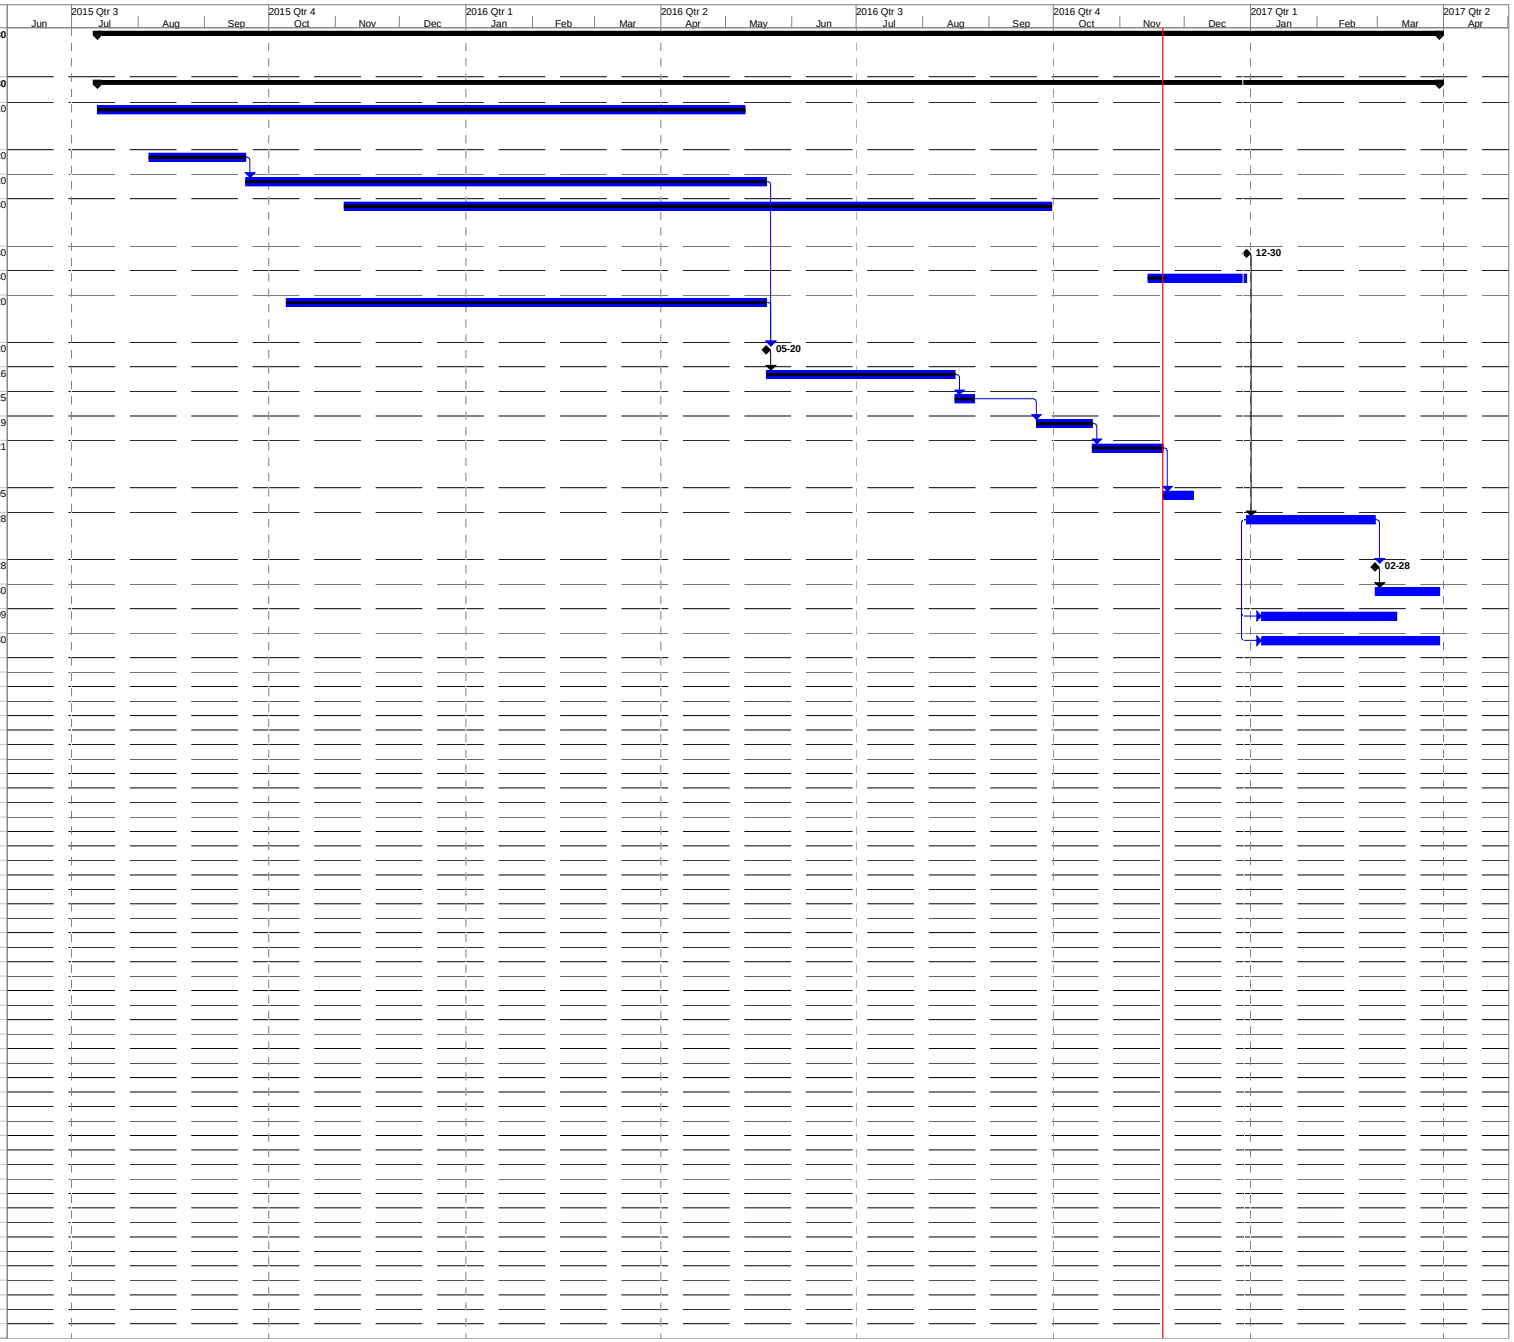

Appendix no. 3 Real property acquisition schedule

Construction of “Krosnowice” - a dry flood control reservoir on Duna Stream

11.02.2016

ID	Nazwa zadania	Start	Finish		2015 Qtr 3			2015 Qtr 4			2016 Qtr 1			2016 Qtr 2			2016 Qtr 3			2016 Qtr 4			2017 Qtr 1			2017 Qtr 2
				Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
